



Airside D Trade Partner Outreach Event

April 23rd, 2024

Hillsborough County Aviation Authority
Tampa International, Peter O. Knight, Plant City and Tampa Executive Airports

CONTRACT GROUPS

 **HENSEL PHELPS**
P.L.L.C.

 **HNTB**

 **BE&K**


 **Gensler**

 Tampa
International
Airport

Agenda

1. Team Introductions
2. Project Overview
3. Bid Package Plan
4. Schedule
5. Prequalification Process
6. DBE Program
7. Q&A

Tampa International Airport – Airside D Project Organization

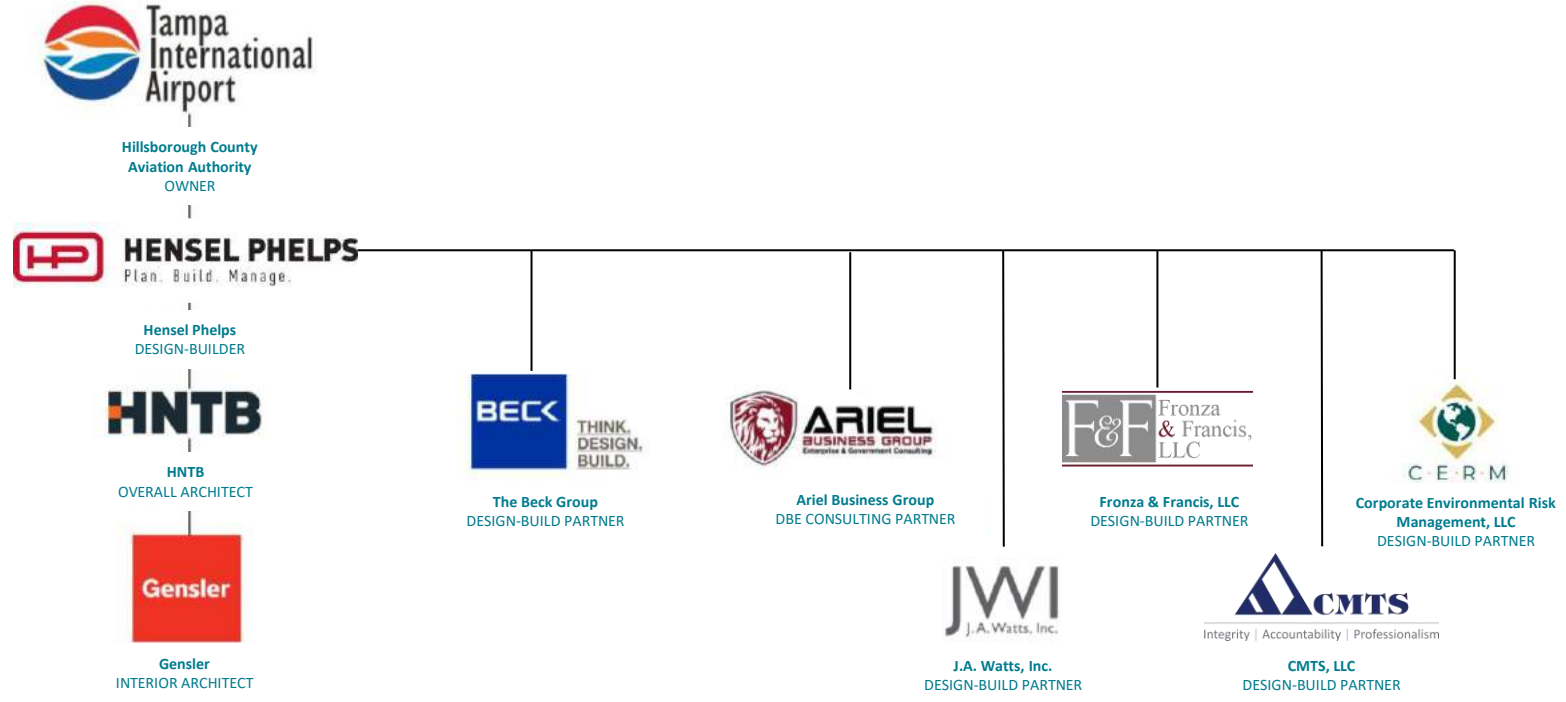

HENSEL PHELPS AND HNTB LEADERSHIP TEAM



**JOHN
SMALLEY**

ENABLING PROJECT
MANAGER
HENSEL PHELPS



**NICK
PETTERSON**

BHS PROJECT MANAGER
HENSEL PHELPS



**JAMAR
LITTLEJOHN**

COORDINATOR OF
SUPPLIER DIVERSITY
HENSEL PHELPS

**SCOTT
STECKLER**

PROJECT MANAGER
FOR DESIGN
HNTB



**GREG
COBB**

ESTIMATING DIRECTOR
HENSEL PHELPS



**ANDREW
ERBRICK**

PRECONSTRUCTION
MANAGER
HENSEL PHELPS



**JOE
GIUNTA**

PROJECT DIRECTOR
HENSEL PHELPS



**DREW
KRIZMAN**

PROJECT MANAGER
FOR CONSTRUCTION
HENSEL PHELPS



**PAT
BRACKMAN**

GENERAL SUPERINTENDENT
FOR CONSTRUCTION
HENSEL PHELPS



**KEVIN
CURRY**

PROJECT SUPERINTENDENT
FOR CONSTRUCTION
HENSEL PHELPS






Airside D Project Overview

- Airside D Building
 - 16 Dual Purpose International / Domestic Gates
 - Holdrooms and Circulation Space
 - Concessions
 - Airline Operations and Support Spaces
 - Airline/Airport Club Spaces
 - TSA Security Screening Checkpoint (SSCP)
 - CBP Federal Inspection Station (FIS)
- Apron Upgrades
 - Existing Apron Demolition
 - Replacement Apron Construction
 - New Hydrant Fueling System
- Elevated Guideway Structure for Shuttle
- Passenger Boarding Bridges (PBB)
- Airline Relocations at the Main Terminal
- Consolidated Checked Baggage Systems – Airsides D/E/F





PROJECT FOOTPRINT AND LOCATION

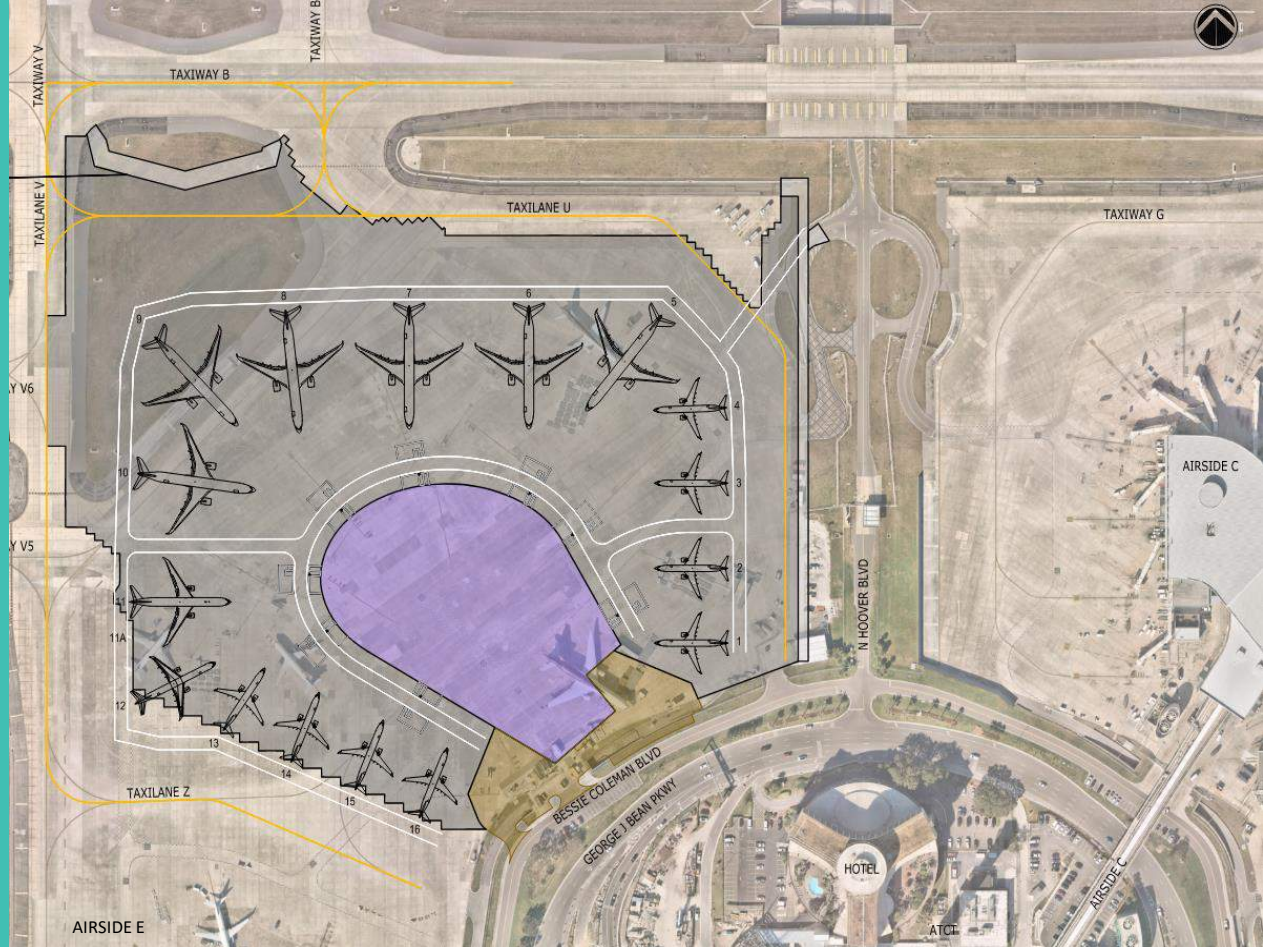

Anticipated Building Elements

- Deep Foundations and Pile Caps
- Steel Frame Building w/ Concrete Slab on Metal Deck
- Curtain Wall Systems
- TPO / Metal Roofing Systems
- Mechanical / Electrical / Plumbing / Fire Protection
 - Central Utility Plant
 - Building Management Systems
- Baggage Handling Systems
- Building Finishes
- Civil / Utilities Scopes
- Apron Demolition and Reconstruction
- Construction Office Compound Development



PROCUREMENT BREAKDOWN



Bid Package Plan – Bid Packages Issued by Hensel Phelps

1. Enabling Package – Q2/Q3 2024
 - A. Office Trailers & FFE
 - B. Early Civil/Utilities
 - C. Pilot Holes
 - D. Site Fencing
 - E. Preliminary Apron Demolition
 - F. Miscellaneous Scopes in Development
2. Baggage Handling System Design/Build – Q3/Q4 2024
3. Deep Foundations – Q1/Q2 2025
4. Core/Shell/MEP/Finishes – Q2/Q3 2025




Bid Package Plan – Invitation to Bid (ITB) Packages Issued by HCAA

1. Apron Demolition/Pavement and Hydrant Fueling – Q1/Q2 2025
2. Elevated Shuttle Guideway – Q1/Q2 2025
3. Passenger Boarding Bridges – Q1/Q2 2025



Airside D Project Schedule

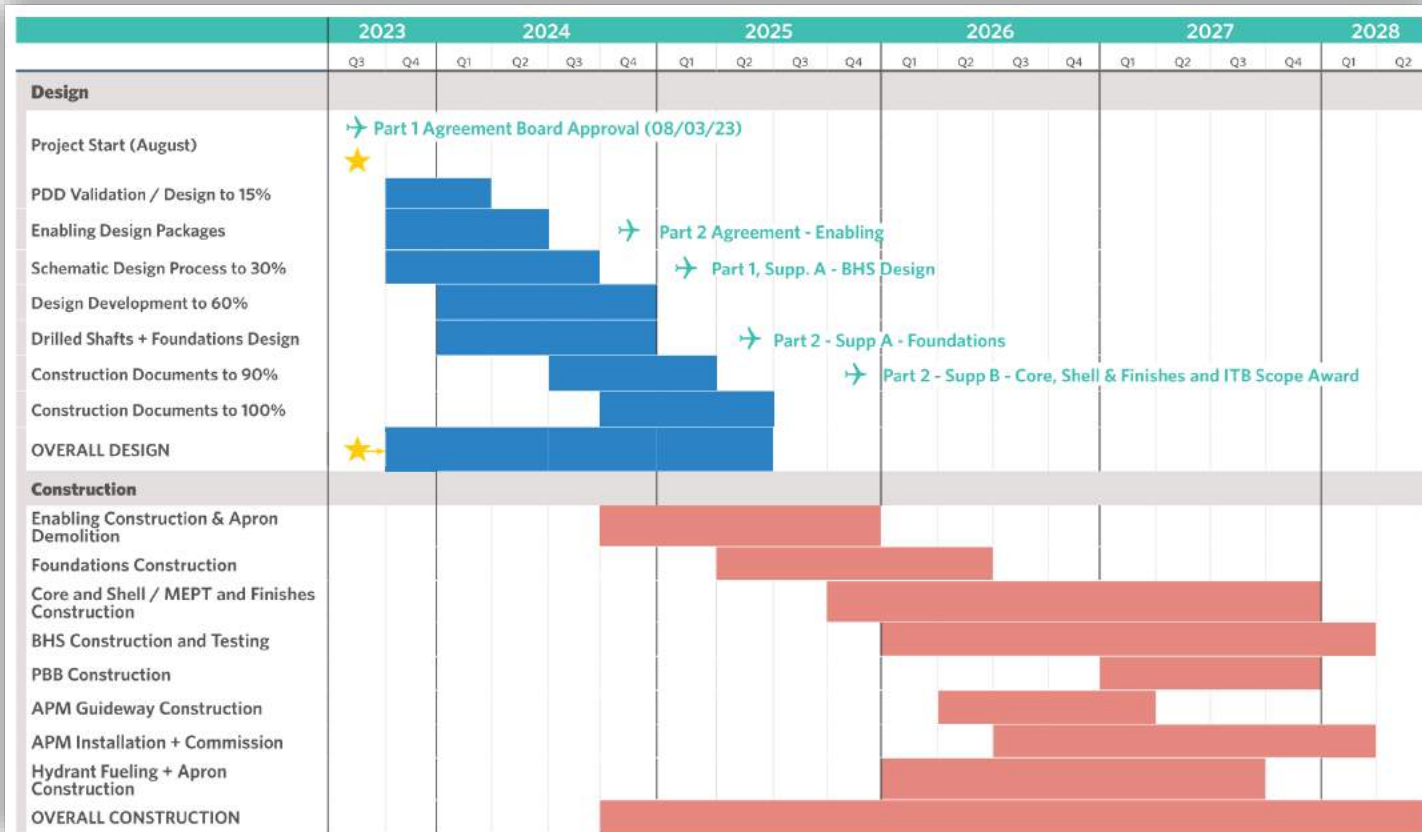

Interested Vendors Registration

- Compass is a comprehensive platform for coordinating Interested Vendors and Subcontractor Prequalification.
- In order to register with Hensel Phelps, subcontractors **must scan and register using the QR Code to begin the process.**



COMPASS
powered by *bespokemetrics*



Interested Vendors Registration

- If the vendor has an account with Compass, they will automatically be added to the Interested Vendors list by logging in using the link.
- If the vendor DOES NOT have an account, they will be directed to setup an account with Compass. Using the link will automatically attach you to this project.



COMPASS
powered by **bespokemetrics**



Interested Vendors Registration

- Prequalification Evaluation:
 - Used for Sorting and Identifying Vendors.
 - Financial information must be shared to Hensel Phelps via Compass.



COMPASS
powered by **bespokemetrics**




Interested Vendors Registration

- Bonding Requirements
 - Subcontractor must submit bonding capability information through Compass.
 - All subcontracts over \$100,000 will require payment and performance bonds.
- DBE Requirements
 - If the subcontractor identifies as DBE, they must submit documentation via Compass.
 - If firms do not submit adequate documentation, they cannot identify as DBE.



Airside D Project Information Website

- For more information about the project and additional links, please check out our website below:
 - <https://tampaairsided.henselphelps.com>

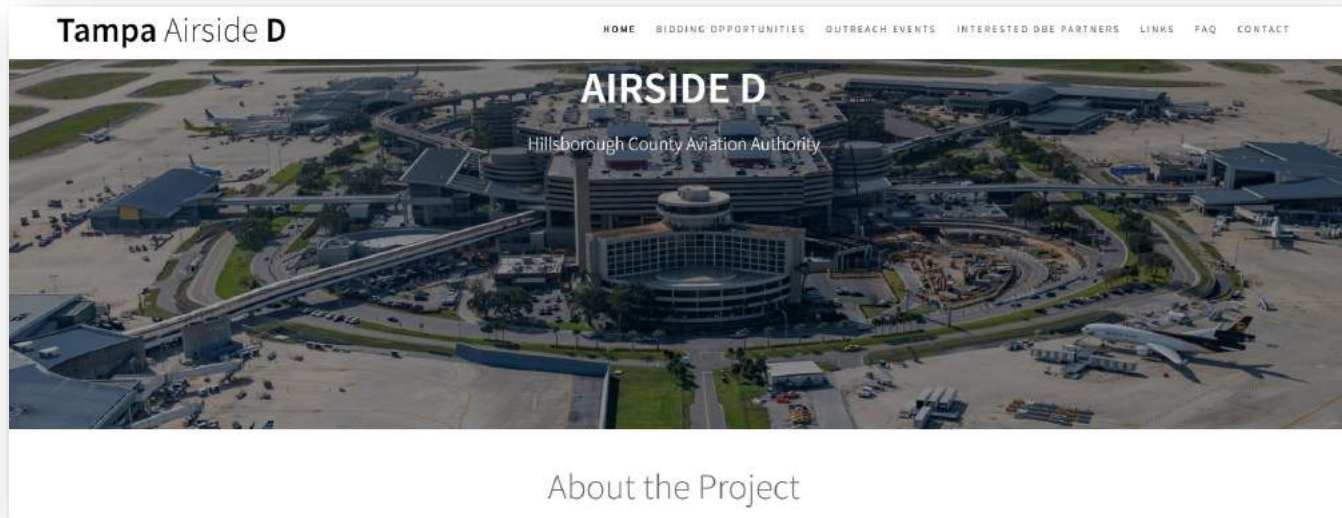

Disadvantaged Business Enterprise (DBE) Project Commitment

Goal 13%



THOMAS HUGGINS, III
President & CEO



"Each trade will have its own contractual requirements for DBE Participation. Zero participation is NOT acceptable."

Disadvantaged Business Enterprise (DBE) Project Commitment

Accepted Certifications

- Disadvantaged Business Enterprise (DBE) ONLY



Florida DBE Certifying Agencies*

- **Hillsborough County Aviation Authority**
- **Florida Department of Transportation**
- Greater Orlando Aviation Authority
- Broward County Office of Economic and Small Business Development
- Jacksonville Transportation Authority
- Lee County Board of County Commissioners
- Palm Beach International Airport
- Miami-Dade International Airport

**This is a partial listing of Florida DBE certifying agencies.*

Disadvantaged Business Enterprise (DBE) Project Commitment

Please email all questions to:

hensel-phelps@arielbusinessgroup.com

